



**ISD #883**  
**Rockford Area Schools**  
**LTFM & Abatement Bond Projects**

**ICS Weekly Progress Report**  
**Friday November 4, 2022**

Address: 6051 Ash Street, Rockford, MN 55373


## **Weeks Ending October 28, 2022**

- 🔧 Continued work @ ES:
  - Installed base course and final wear course of pavement
  - Striped pavement for parking stalls
  - Poured concrete in light pole bases
  - Prepped surrounding grades for final landscaping
- 🔧 Continued work @ MS:
  - Installed final wear course of pavement
  - Finished installation of light poles
  - Striped pavement for parking stalls
  - Installed Basketball Hoops

## **Week Ending November 04, 2022**

- 🔧 Continued work @ ES:
  - Installed light poles
  - Installed basketball hoops
  - Installed plantings and laid final landscaping
  - Cleaned materials from site
  - Working on final punch list items
- 🔧 Continued work @ MS:
  - Installed temporary railing
  - Cleaned materials from site
  - Working on final punch list items

## Construction Progress Photos – MS

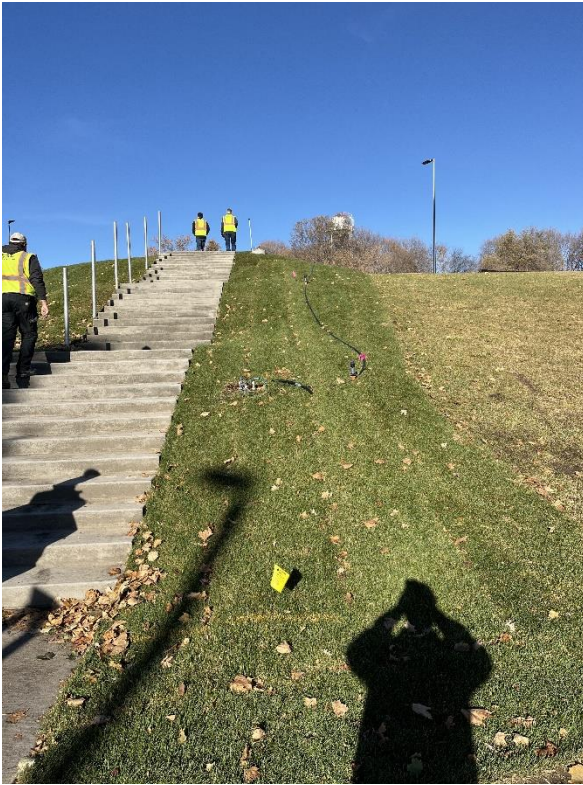

**Temp railing being installed along stairwell**



**Main parking lot lights installed – waiting for walking trail light poles**



**Basketball hoops installed**




**Final striping installed**

## Construction Progress Photos – ES




**Sidewalks have been poured**

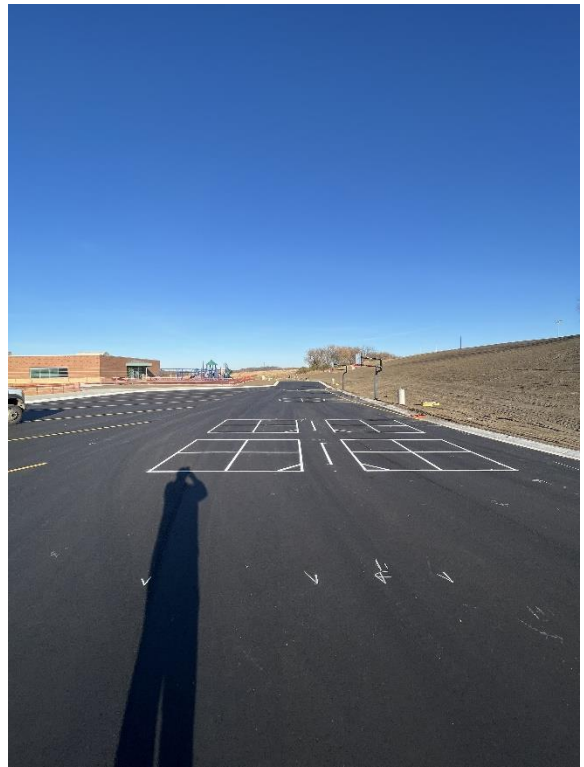

**Parking lot striping complete**



**Basketball hoops installed**

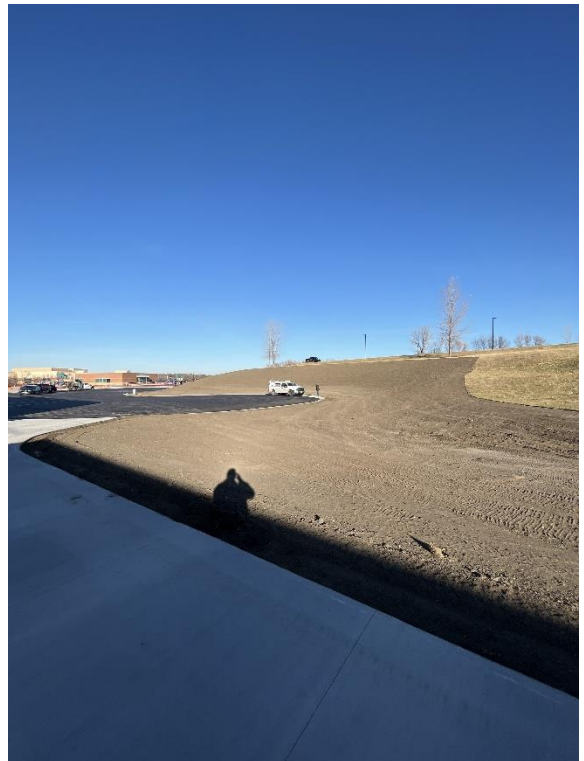

**Final grading complete and  
ready for sod**
